REQUEST FOR BOARD ACTION HENDERSON COUNTY BOARD OF COMMISSIONERS

MEETING DATE:

September 8, 2009

SUBJECT:

CAPITAL / FACILITIES STATUS REPORTS:

Henderson County Public Schools

Apple Valley/North Henderson High School

HVAC Pipe Upgrade Project

ATTACHMENTS:

YES

SUMMARY OF REQUEST:

The attached Status Reports are provided for the Board's information.

BOARD ACTION REQUESTED:


No action required; for information only.

SUGGESTED MOTION:

No action required; for information only.

HCPS CAPITAL PROJECTS STATUS REPORT: AUGUST, 2009

JOB NO.	PROJECT NO.	SCHOOL	CATEGORY	PROJECT COMPLETE?	ESTIMATED COST		 UGUST 2009 PENDITURES
NOT ASSIGNED	8-C-HVE	Hendersonville Elem	Security - locks	Yes	\$	10,000.00	\$ 2,652.41
NOT ASSIGNED	20-C-WHH	West Henderson	Building Repair	No	\$	250,000.00	\$ 94,965.52
NOT ASSIGNED	42-C-BAL	Balfour	Door replacement	Yes	\$	5,000.00	\$ 4,751.27
NOT ASSIGNED	5-C-WHH	West Henderson	Roof Projects	No	\$	120,000.00	\$ 72,142.00
				TOTALS:	\$	385,000.00	\$ 174,511.20
TOTAL EXPENDITURES FOR AUGUST, 2009:						\$ 174,511.20	

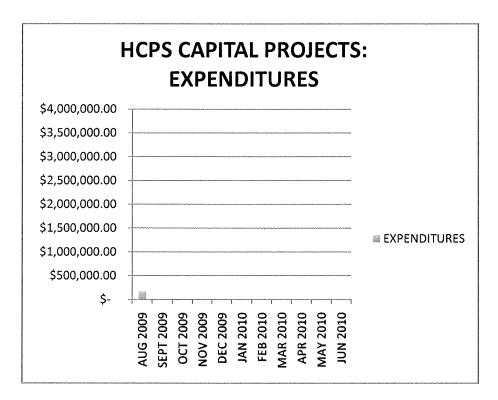


SNAPSHOT:		
# of HCPS Capital Projects Complete:	2	
% of Budget spent as of Report Date:	4.36%	
Total Dollar Amount spent as of Report Date:	\$ 174,511.20	
Total Savings in Estimated Cost over Actual Cost	100000000000000000000000000000000000000	
(applies ONLY to completed Projects Projects that are not 100% complete are not included in this calculation):	\$ 7,596.32	

^{*}NOTE: The HCPS Capital Project List originally included 115 projects. HCPS completed 3 of these projects and partially completed 1 other project prior to the close of FY2009 with either salvaged materials or FY2009 funds. Three projects were removed to arrive at the summary presented above.

HCPS - APPLE VALLEY/NORTH HENDERSON HIGH SCHOOL HVAC PIPE UPGRADE PROJECT STATUS REPORT: AUGUST, 2009

DESCRIPTION OF EXPENDITURE		AMOUNT	
Engineering Fees	\$	43,051.50	
Building Permit Fees	\$	3,122.00	
Geotechnical Services	\$	2,900.00	
TOTAL EXPENDITURES:	AUGUST, 2009 \$	49,073.50	

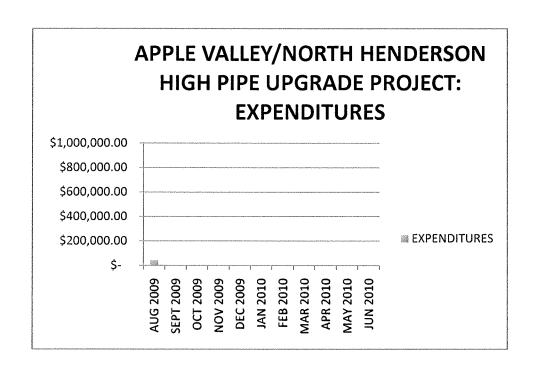

SNAPSHOT:	
Total Budgeted Dollars for Project:	\$ 1,000,000.00
Total Dollars spent as of Report date:	\$ 49,073.50
% of Budget spent as of Report date:	4.91%
% of Budget remaining as of Report date:	95.09%
